


M11 Junction 8 Improvement scheme Milestones for project completion

Ref	Location	Works required	Impact	Estimated	
				Start	Finish
1	Central reservation from junction with Dunmow Road	Construction of central reservation, full road formation, asphalt, ducting, lighting, signage and connections for illuminated signs	Reduction of lanes	Ongoing	early March
2	Gantry install on southbound exit slip	Installation of overhead gantry	Night-time road closure of exit slip with diversion in place	19/02/2024	24/02/2024
3	Birchanger Lane (from the junction with Bishop's Stortford bypass)	Installation of loops for signals, surfacing and lining	Night-time road closure	Early-March	Mid-March
4	A120 from Dunmow Road junction to M11 roundabout (including the Birchanger services) and also West towards Stansted Road	Carriageway final surfacing and ancillary verge works	Night-time road closures	Mid-March	Late-March
5	A1250 Dunmow Road	Carriageway surfacing, reinstatement of bus stop and verge works	Night-time road closures and narrow lanes	Mid-April	Late-April
6	A120 east of Dunmow Road	Completion of traffic signal installation, ducting work for connections ahead of commissioning	TBC	Early-May	Mid-May
7	A1250, A120, Birchanger Lane	Planting of hedges, trees and shrubbery	No traffic management impact, possible footway closure	April	Early May
8	Various locations	Installation of lighting columns	Potential night-time lane closures and reduction of lanes	Ongoing	Early May

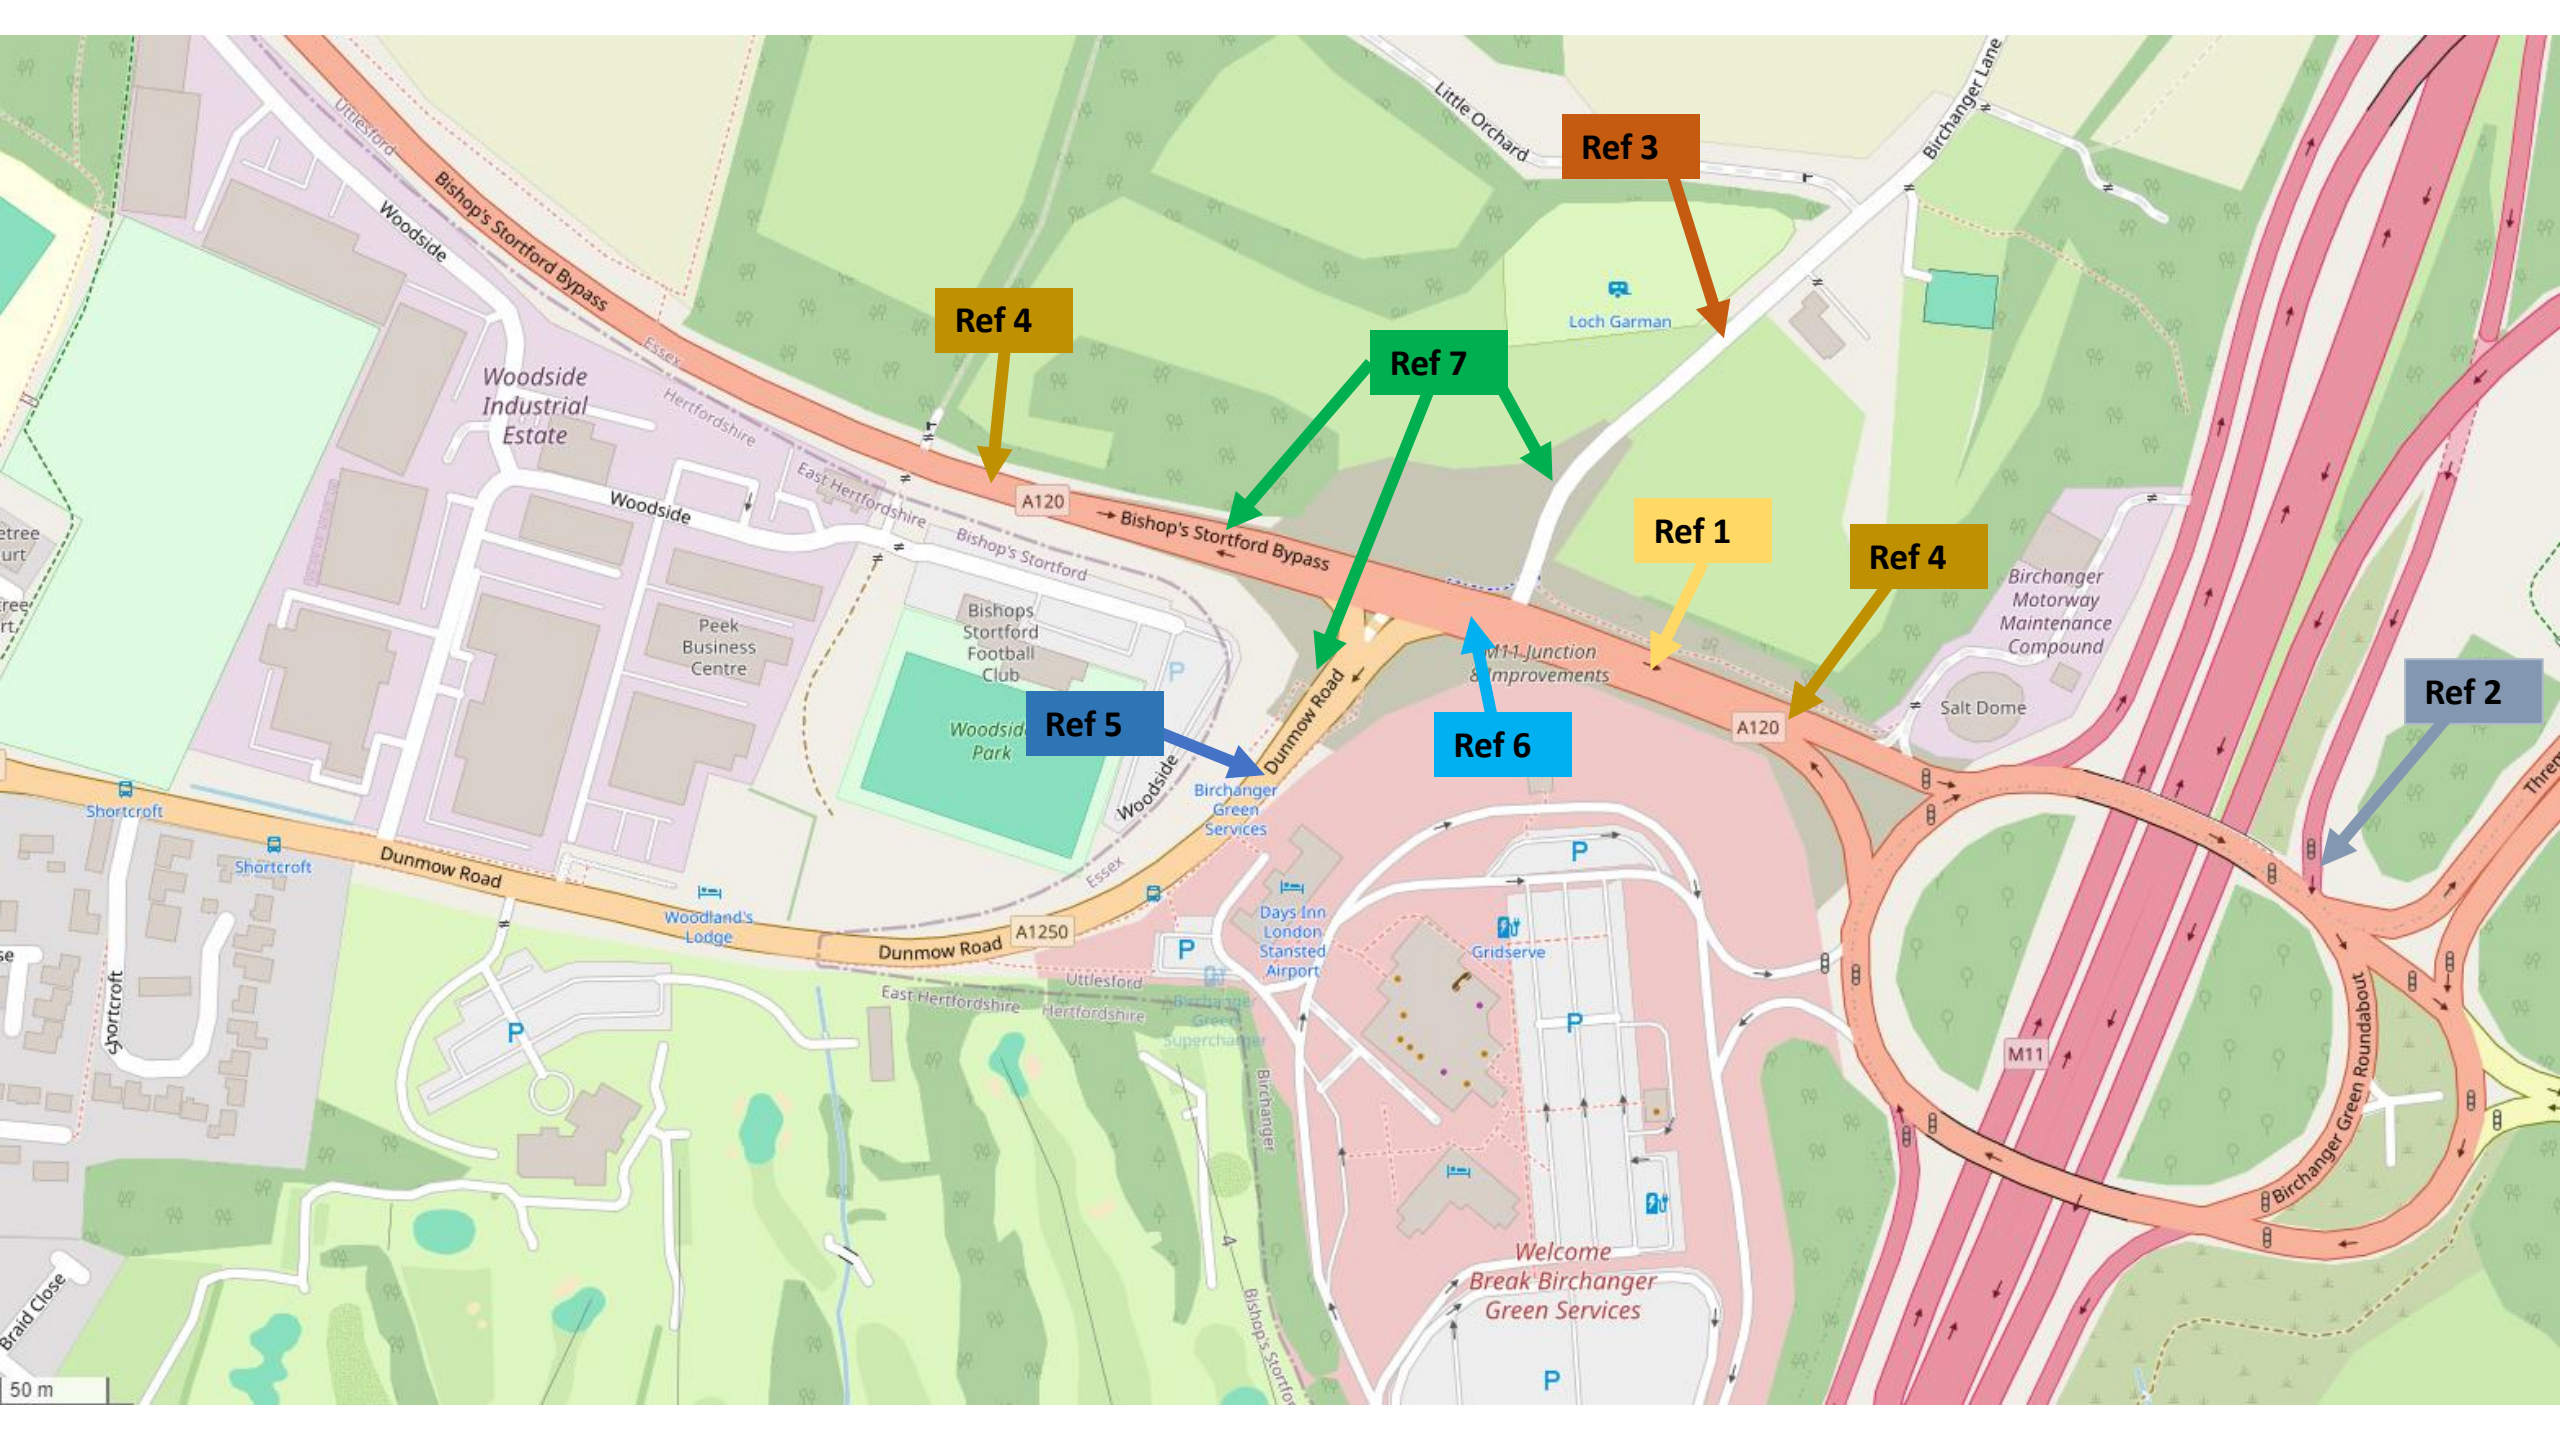

Ref 3

Ref 4

Ref 7

Ref 1

Ref 4

Ref 2

Ref 5

Ref 6

50 m
